



2024 Street Improvement Project Construction Update #8

Current Events

The Contractor has completed paving the majority of the roadways north of 33rd Avenue. Roosevelt Street, which required complete pavement removal and replacement, still requires paving the last layer of asphalt.

The Contractor has completed milling the majority of the roadways south of 33rd Ave NE this week.

See reverse for project location map.

Future Events

The Contractor is anticipated to complete the remaining paving operation along Roosevelt Street north of 33rd Thursday, August 15th, weather permitting.

The Contractor is anticipated to complete project clean up along roadway south of 33rd Avenue Monday, August 12th and Tuesday, August 13th with adjustments to storm and sanitary manholes and water gate valves the remainder of the week. The Contractor is anticipated to complete the remaining milling operations along Roosevelt Street south of 33rd Avenue Wednesday, August 14th. Final paving along the roadway south of 33rd is anticipated to be completed the week of August 19th, weather permitting.

The Contractor has tentatively scheduled the removal and replacement of deficient sidewalk within Salo Park the week of August 19th and the trail and parking lot improvements within Silver Point Park in September.

The above schedule is tentative and is subject to change due to weather or scheduling conflicts.

Roadway Paving

Following paving of your roadway:

- Do not turn your wheels at a stop condition on a newly paved road to avoid leaving impressions in the pavement.
- As soon as the rollers have made a couple of passes on the fresh asphalt you may drive on it.

Lawn Irrigation and Pet Fences

If you have a lawn irrigation system or pet fence within the City right-of-way, please mark the location of the sprinkler heads before construction. This will allow the contractor to take precautionary measures to protect your irrigation system and pet fence or identify where to replace the system if it cannot be avoided.

Tips of the Week

- Please observe posted detour and warning signs.
- Slow down and watch for uneven surfaces.
- Stay alert! Watch for signs, equipment, and workers.
- Please remind children to stay away from the construction site, equipment, and stockpiles of materials.
- Access through the site may change throughout the day as construction progresses; your patience is appreciated.


Project Contacts

Onsite Project Representative: Kate Achenbach (651) 302-3367

Project Manager: Katie Koscielak (612) 282-3641

City Engineer: Justin Messner (612) 388-9652

Director of Public Works: Jeremy Gumke (612) 782-3441

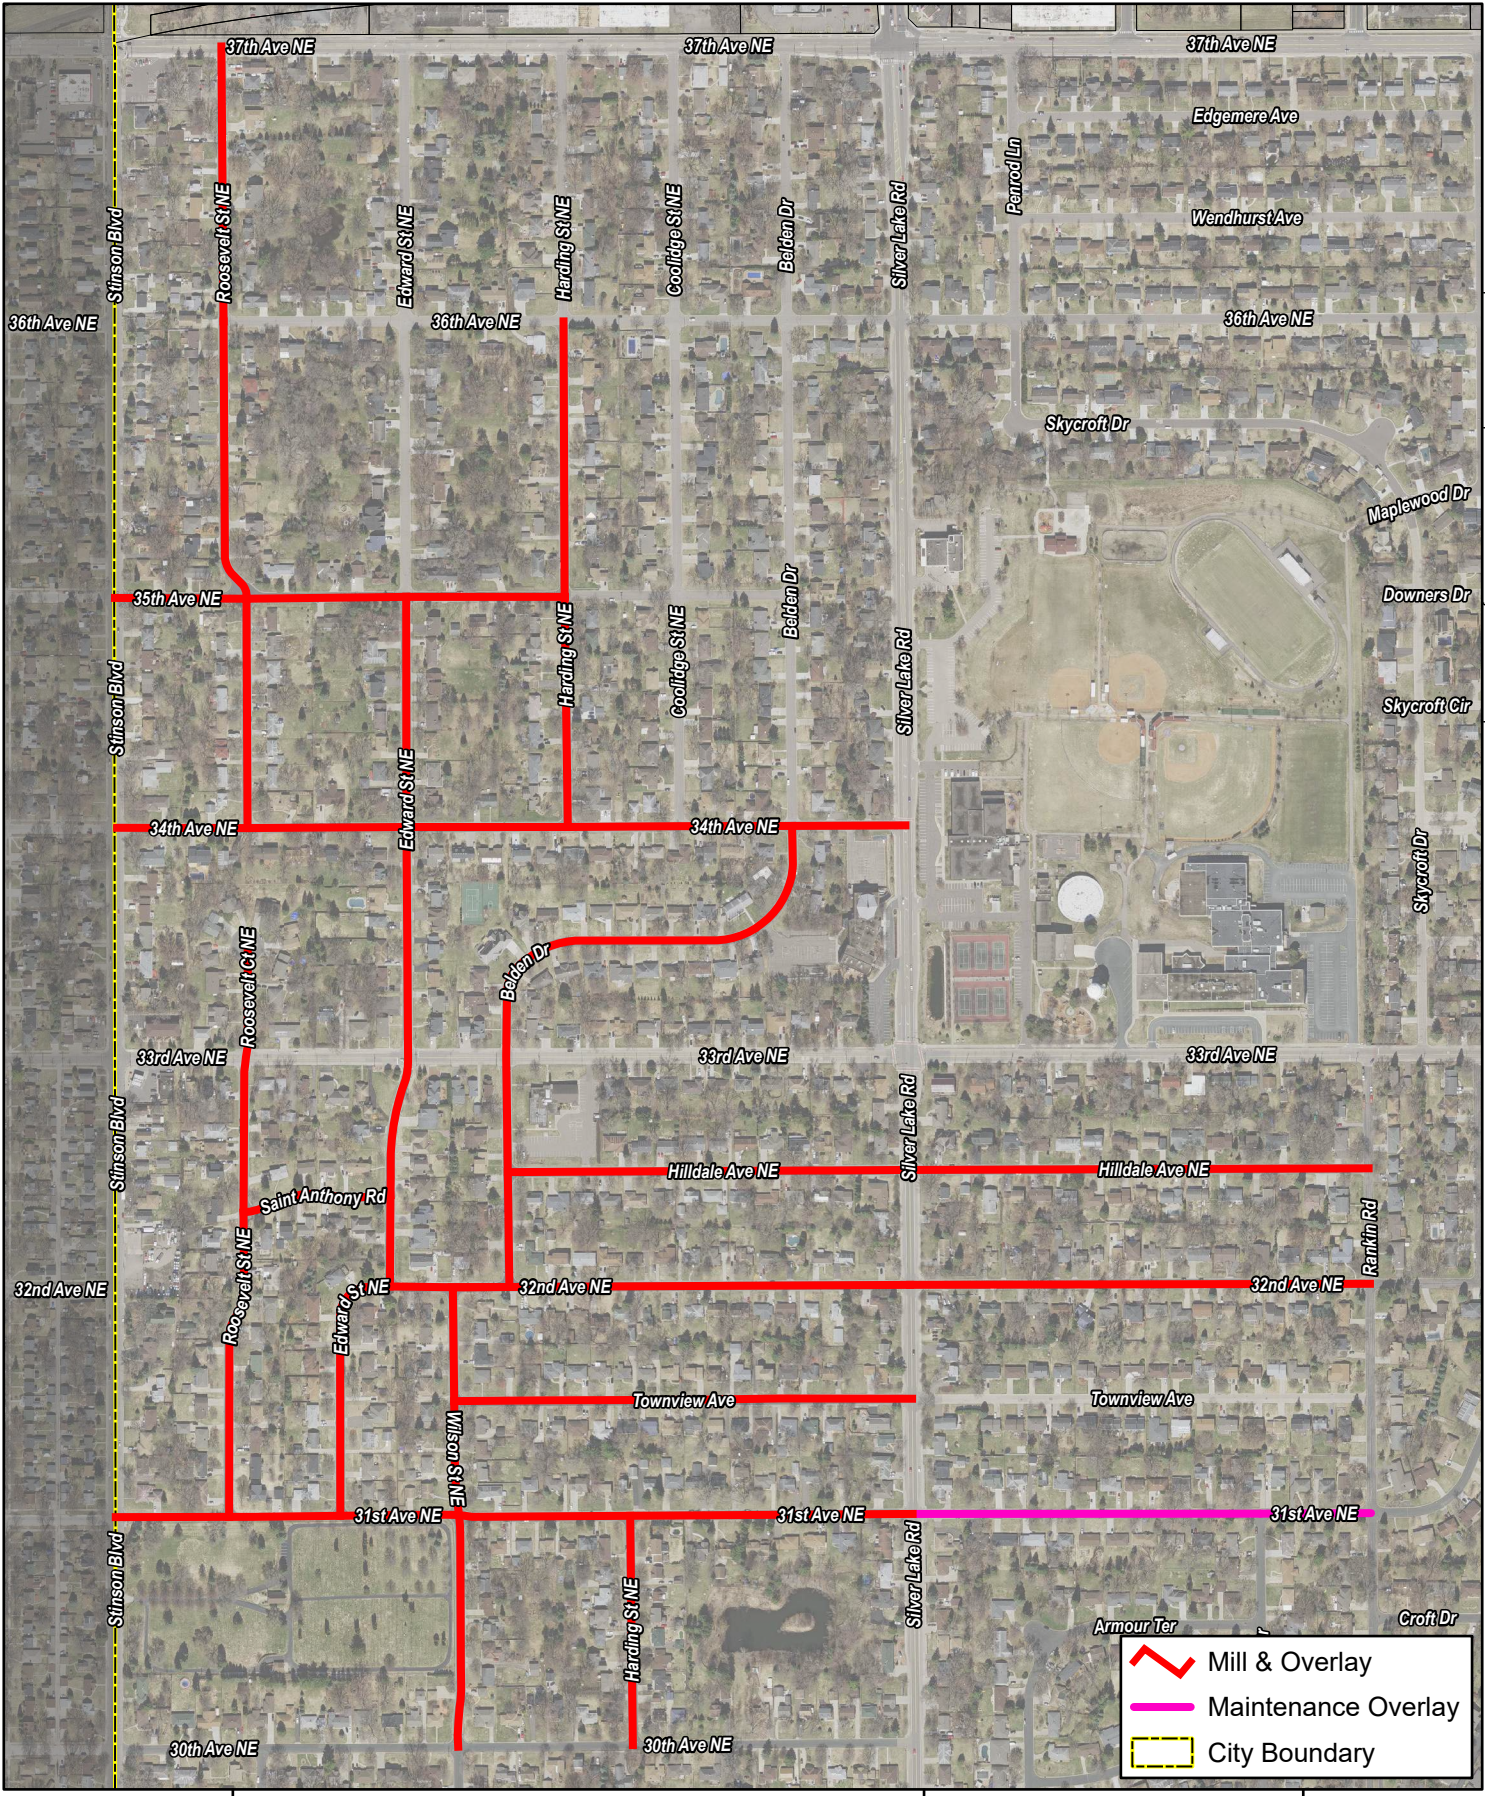

2024 STREET IMPROVEMENT PROJECT
 FIGURE 1 - LOCATION MAP
 ST. ANTHONY VILLAGE, MINNESOTA

